

Compass Spectrometer / CERN


Thu 30/9/99

ID	Task Name	Duration	Start	1999												2000												2001					
				D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M
1	compass	615 days	Mon 28/12/98	[Project Summary Bar]																													
2	DAQ	547 days	Thu 1/4/99	[DAQ Bar]																													
1	TCS	246 days	Mon 3/5/99	[TCS Bar]																													
2	Receiver prototype	92 days	Mon 3/5/99	[Receiver prototype Bar]																													
3	development	50 days	Mon 3/5/99	[Receiver prototype sub-task]																													
4	layout	14 days	Mon 12/7/99	[Receiver prototype sub-task]																													
5	PCB production	14 days	Fri 30/7/99	[Receiver prototype sub-task]																													
6	assembly and debugging	14 days	Thu 19/8/99	[Receiver prototype sub-task]																													
7	Controller prototype	69 days	Thu 3/6/99	[Controller prototype Bar]																													
8	development	32 days	Thu 3/6/99	[Controller prototype sub-task]																													
9	layout	14 days	Fri 16/7/99	[Controller prototype sub-task]																													
10	PCB production	14 days	Thu 5/8/99	[Controller prototype sub-task]																													
11	assembly and debugging	10 days	Wed 25/8/99	[Controller prototype sub-task]																													
12	Implementation	0 days	Tue 7/9/99	[Implementation Milestone]																													
13	System test	30 days	Wed 8/9/99	[Implementation sub-task]																													
14	Controller firmware update	31 days	Wed 20/10/99	[Implementation sub-task]																													
15	Receiver final version	103 days	Wed 20/10/99	[Receiver final version Bar]																													
16	design	30 days	Wed 20/10/99	[Receiver final version sub-task]																													
17	orders	0 days	Tue 30/11/99	[Orders Milestone]																													

Project: Compass Spectrometer Date: Mon 2/8/99 Co-ordinator: Gerhard Mallot /CERN	Task		Summary		Rolled Up Progress	
	Split		Rolled Up Task		External Tasks	
	Progress		Rolled Up Split		Project Summary	
	Milestone		Rolled Up Milestone			

Compass Spectrometer / CERN

Thu 30/9/99

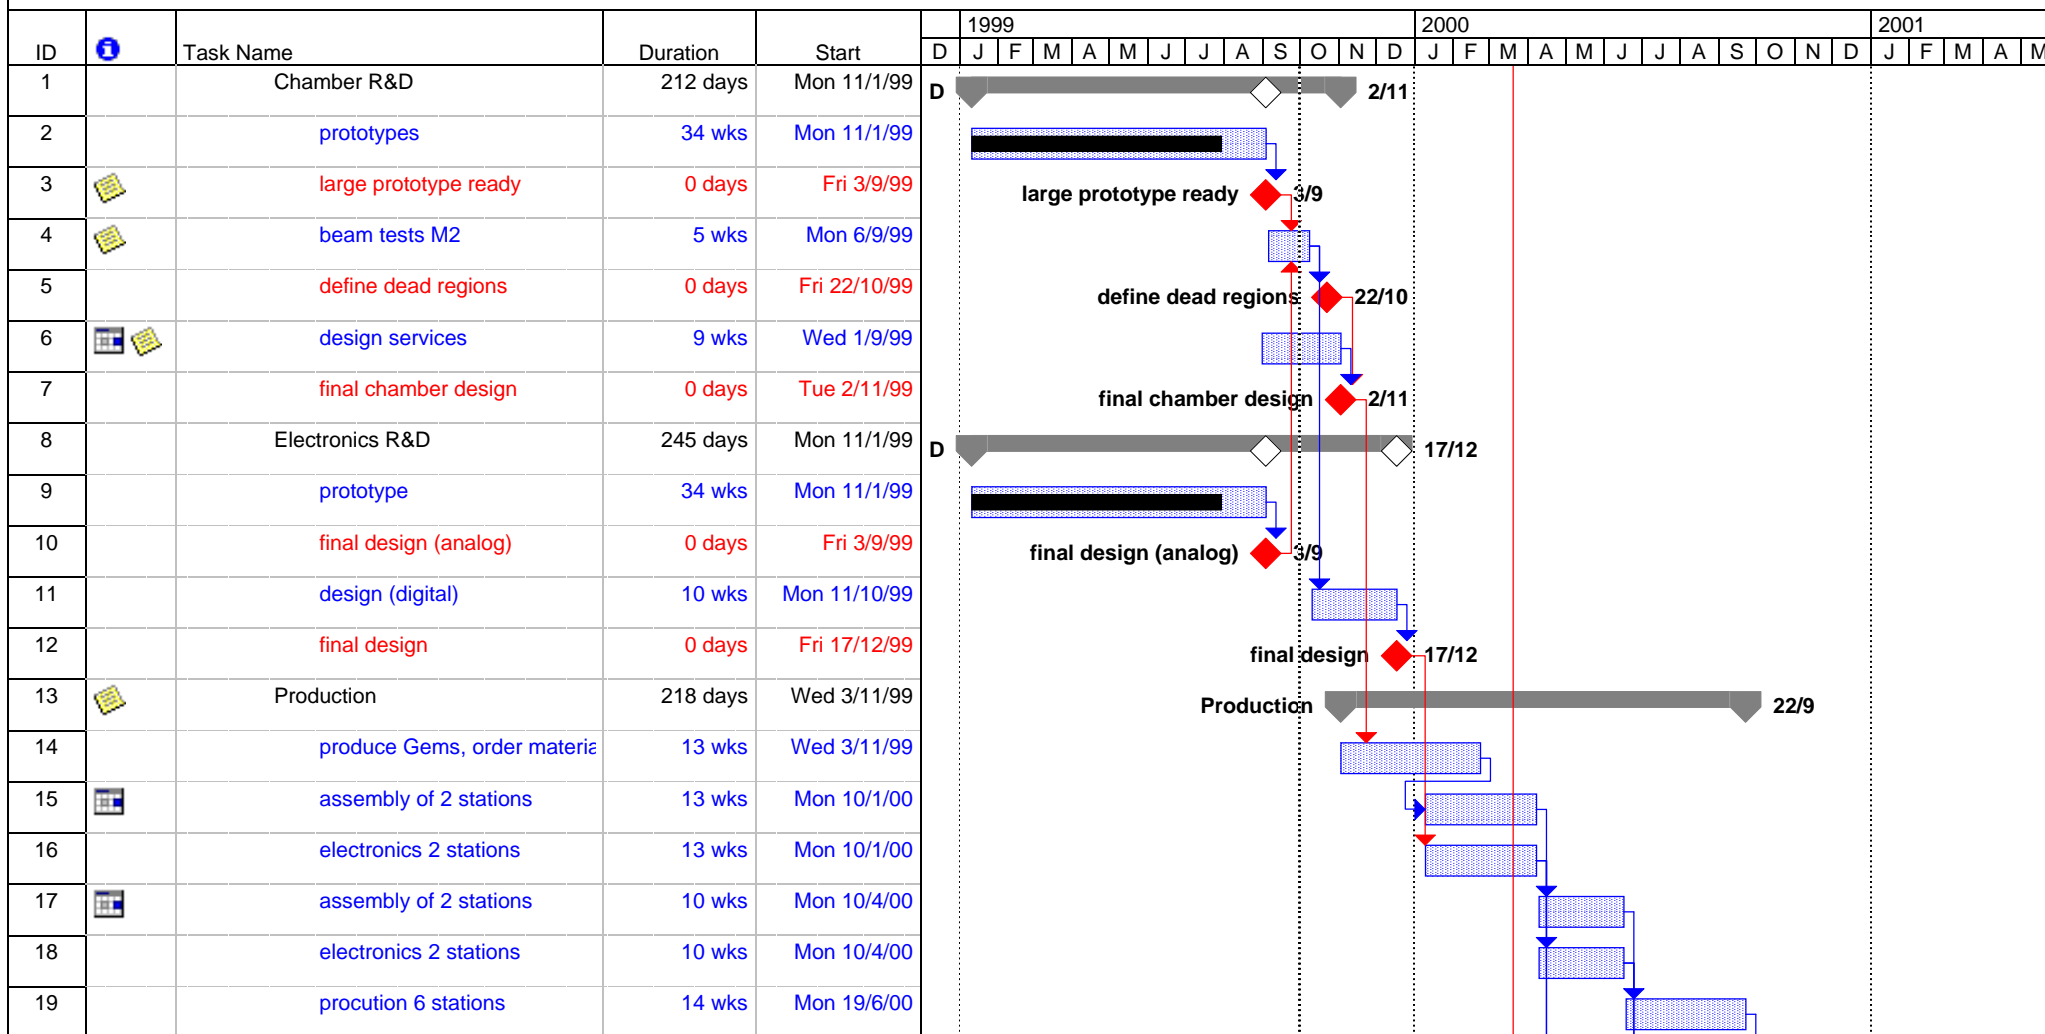

Project: Compass Spectrometer Date: Mon 2/8/99 Co-ordinator: Gerhard Mallot /CERN	Task	Summary	Rolled Up Progress
	Split	Rolled Up Task	External Tasks
	Progress	Rolled Up Split	Project Summary
	Milestone	Rolled Up Milestone	

Compass Spectrometer / CERN

Thu 30/9/99


ID	Task Name	Duration	Start	1999												2000												2001				
				D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A
8	all 480 modules ready	0 days	Wed 15/9/99	all 480 modules ready ◆ 15/9																												
9	HCAL1 Design	150 days	Mon 11/1/99	◆ 6/8																												
10	design phase 1	20 wks	Mon 11/1/99																													
11	design phase 2	8 wks	Mon 31/5/99																													
12	approval of design	2 wks	Mon 26/7/99																													
13	design complete	0 days	Fri 6/8/99	design complete ◆ 6/8																												
14	Production frame	114 days	Mon 9/8/99	◆ 28/1																												
15	production	82 days	Mon 9/8/99																													
16	production finished	0 days	Tue 30/11/99	production finished ◆ 30/11																												
17	preassembly	22 days	Wed 1/12/99																													
18	transport to CERN	2 wks	Mon 17/1/00																													
19	HCAL1 at CERN	0 days	Fri 28/1/00	HCAL1 at CERN ◆ 28/1																												
20	Installation	30 days	Tue 29/2/00													◆ 10/4																
21	assembly	2 wks	Tue 15/2/00																													
22	chariot and frame	2 wks	Tue 29/2/00																													
23	modules	3 wks	Tue 14/3/00																													
24	cables	1 wk	Tue 4/4/00																													
25	Readout	100 days	Mon 25/10/99	◆ 27/3																												
26	final design readout	0 days	Fri 22/10/99	final design readout ◆ 22/10																												

Project: Compass Spectrometer
 Date: Mon 2/8/99
 Co-ordinator: Gerhard Mallot /CERN

Task		Summary		Rolled Up Progress	
Split		Rolled Up Task		External Tasks	
Progress		Rolled Up Split		Project Summary	
Milestone		Rolled Up Milestone			

Compass Spectrometer / CERN


Thu 30/9/99

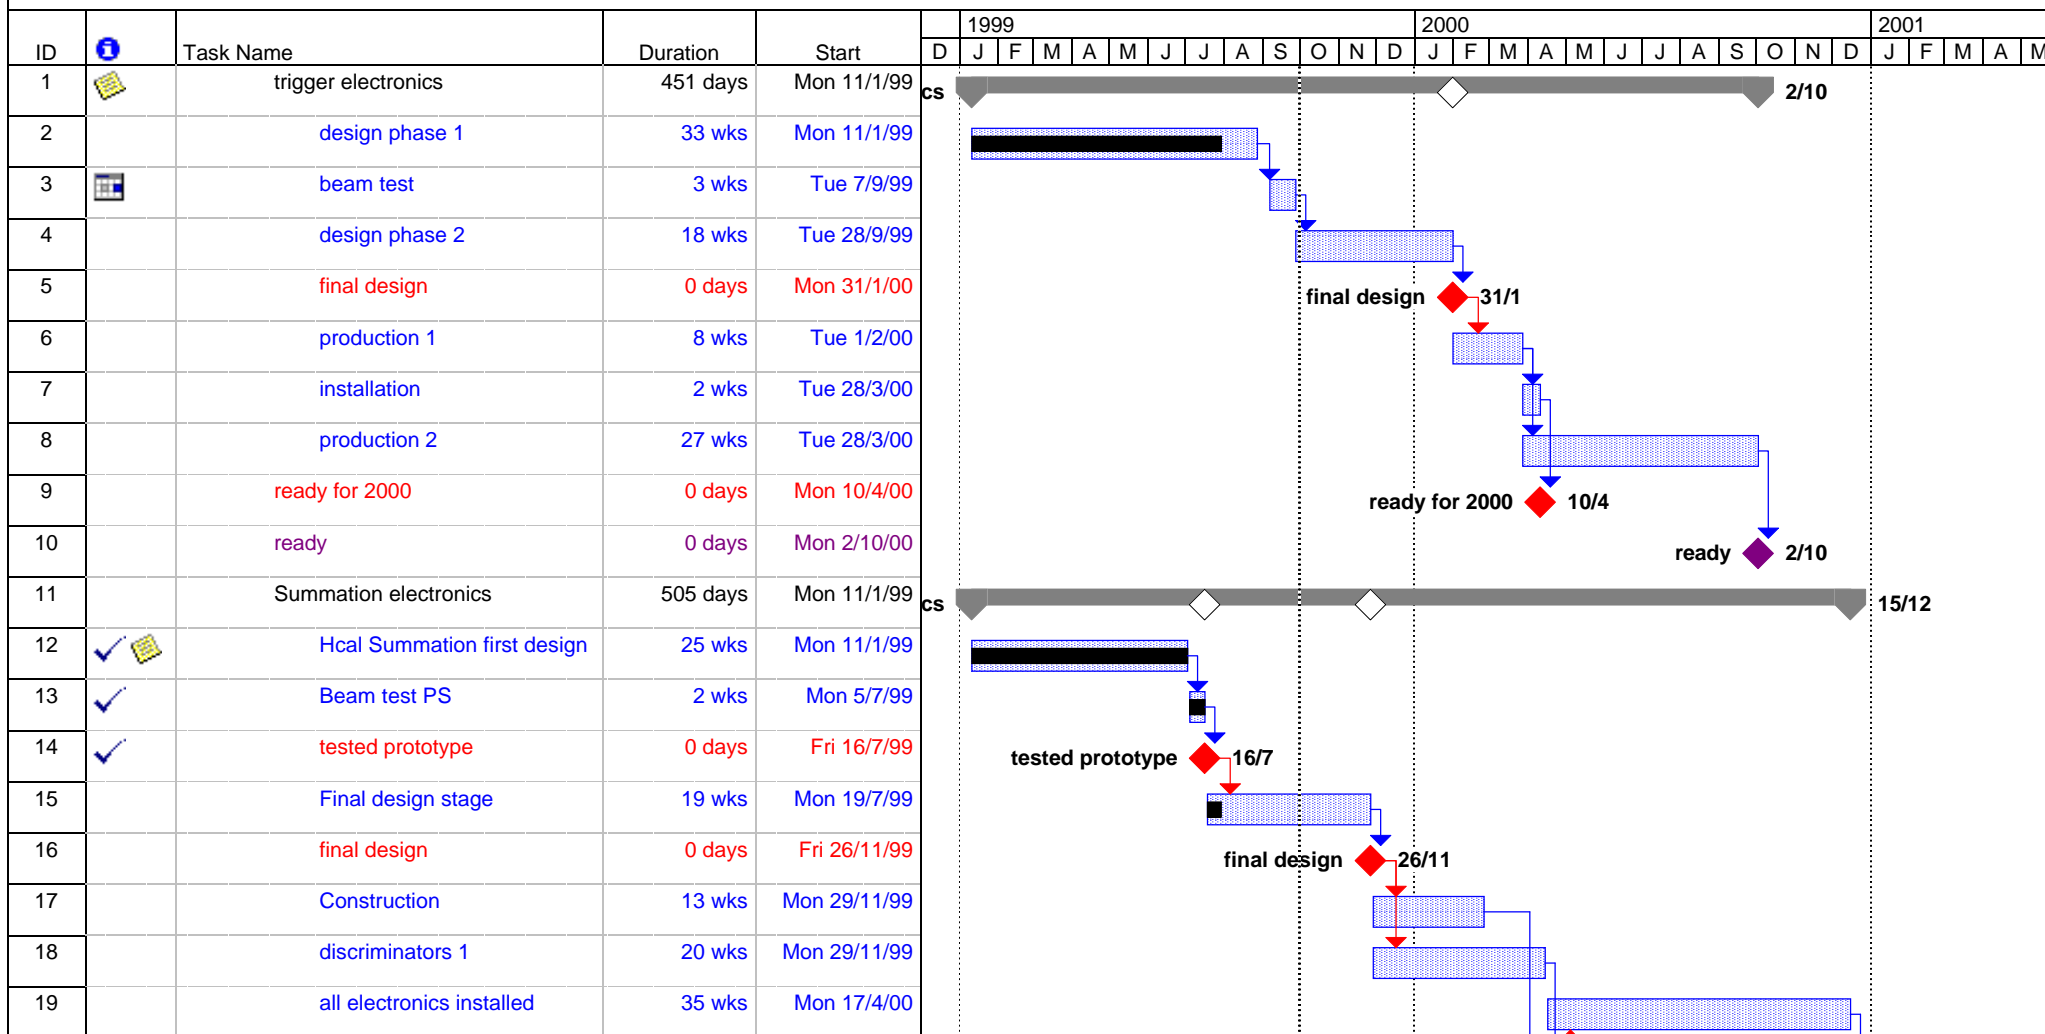

Project: Compass Spectrometer Date: Mon 2/8/99 Co-ordinator: Gerhard Mallot /CERN	Task		Summary		Rolled Up Progress	
	Split		Rolled Up Task		External Tasks	
	Progress		Rolled Up Split		Project Summary	
	Milestone		Rolled Up Milestone			

Compass Spectrometer / CERN

Thu 30/9/99

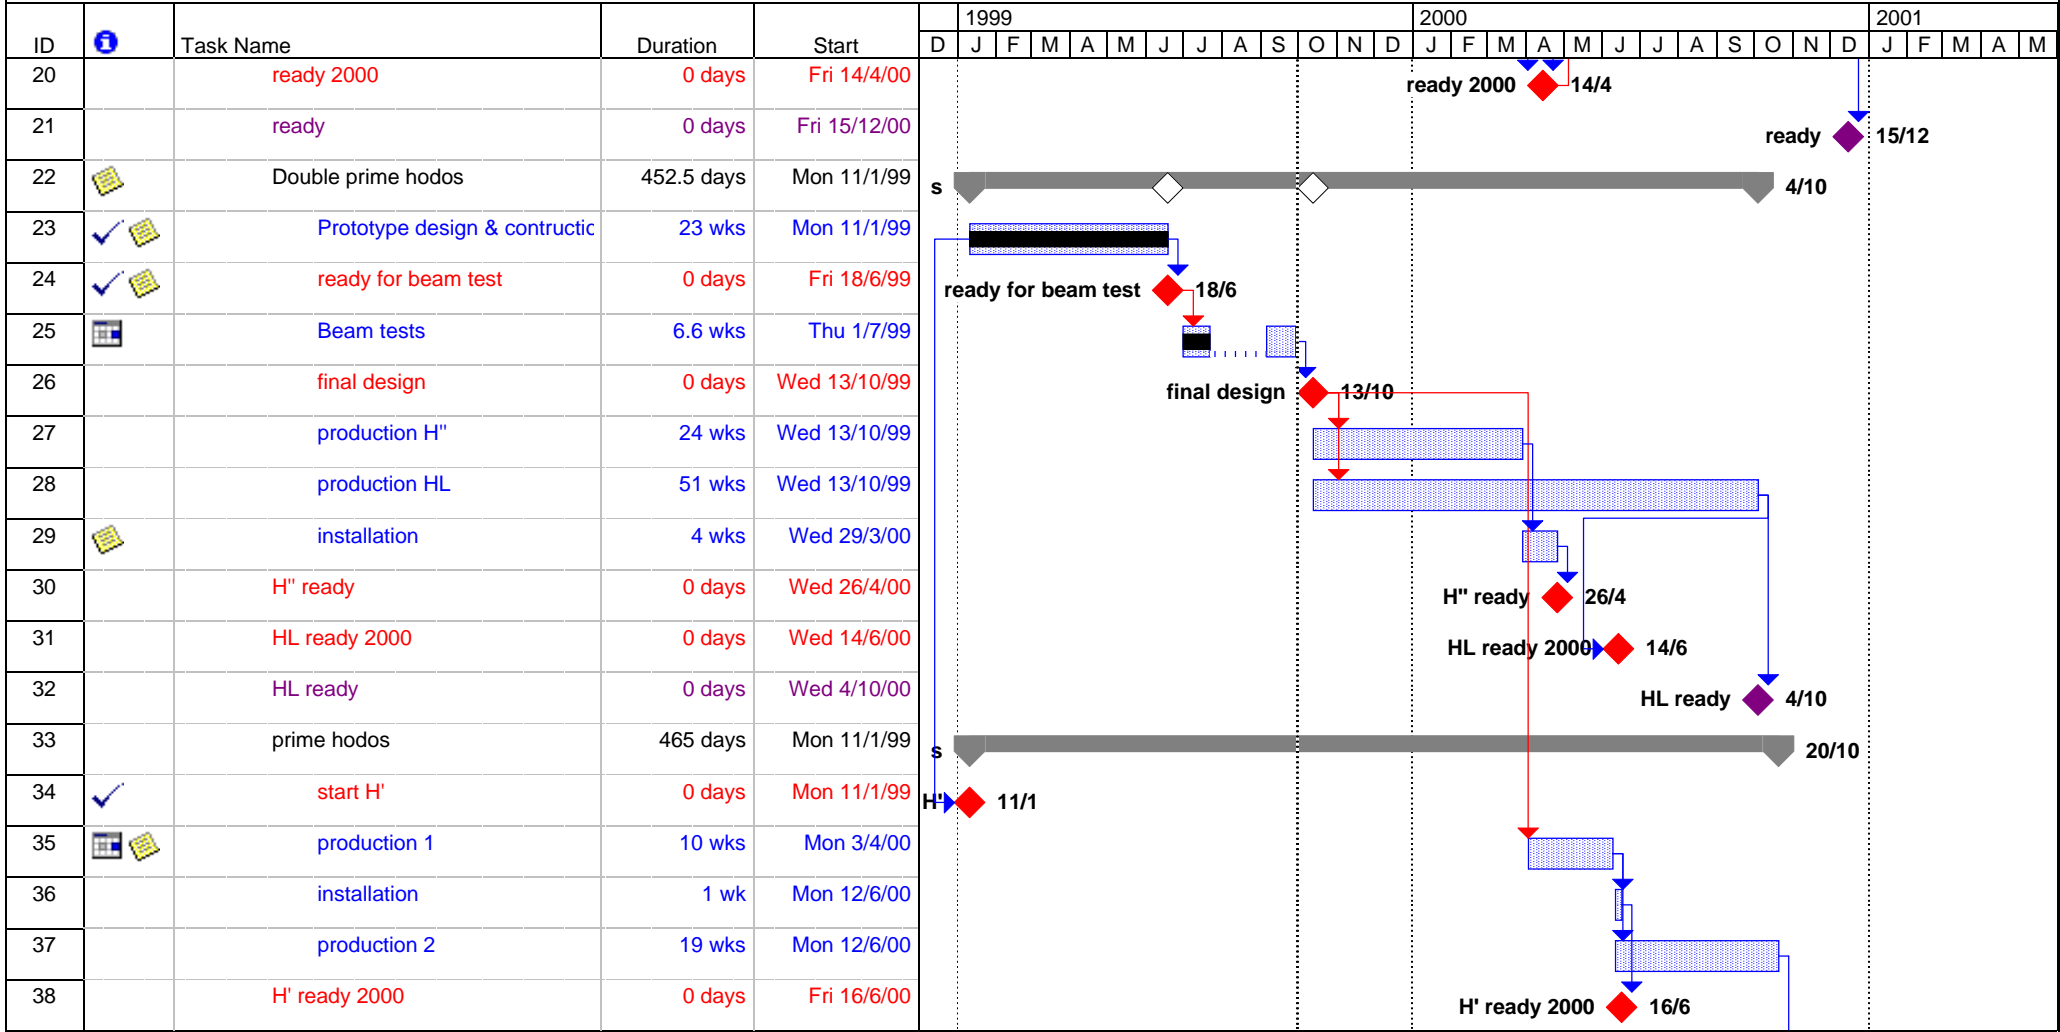

Project: Compass Spectrometer Date: Mon 2/8/99 Co-ordinator: Gerhard Mallot /CERN	Task [Task Bar] Split [Dotted Bar] Progress [Solid Bar] Milestone [Red Diamond]	Summary [Arrow Bar] Rolled Up Task [Hatched Bar] Rolled Up Split [Dotted Bar] Rolled Up Milestone [White Diamond]	Rolled Up Progress [Thick Solid Bar] External Tasks [Grey Bar] Project Summary [Green Arrow Bar]
---	--	--	---

Compass Spectrometer / CERN


Thu 30/9/99

ID	Task Name	Duration	Start	1999												2000												2001																					
				D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M																
16	Mecanical integratic	1 wk	Mon 19/7/99									█																																					
17	CMS components p	6 wks	Mon 10/5/99									█																																					
18	CMS components c	1 wk	Mon 26/7/99																																														
19	Lab tests	2 wks	Mon 2/8/99																																														
20	SAT FEE	65 days	Mon 24/5/99																																														
21	SFE16 board v.20	45 days	Mon 24/5/99																																														
22	Fabrication	6 wks	Mon 24/5/99																																														
23	Lab tests	3 wks	Mon 5/7/99																																														
24	FE board SFE16 v.21	20 days	Mon 26/7/99																																														
25	Fabrication	3 wks	Mon 26/7/99																																														
26	Lab Tests	1 wk	Mon 16/8/99																																														
27	M2 TESTS	30 days	Mon 23/8/99																																														
28	Final integration	1 wk	Mon 23/8/99																																														
29	Lab Tests	1 wk	Mon 30/8/99																																														
30	M2 (SPS) septembre	4 wks	Mon 6/9/99																																														
31	GLOBAL FEE SYSTEM	145 days	Mon 12/7/99																																														
32	Tests Catch+F1 bo	24 wks	Mon 12/7/99																																														
33	Threshold control b	19 wks	Mon 23/8/99																																														
34	Tests FEE system	4 wks	Mon 3/1/00																																														

Project: Compass Spectrometer Date: Mon 2/8/99 Co-ordinator: Gerhard Mallot /CERN	Task Split Progress Milestone	Summary Rolled Up Task Rolled Up Split Rolled Up Milestone	Rolled Up Progress External Tasks Project Summary
---	--	---	---

Compass Spectrometer / CERN


Thu 30/9/99

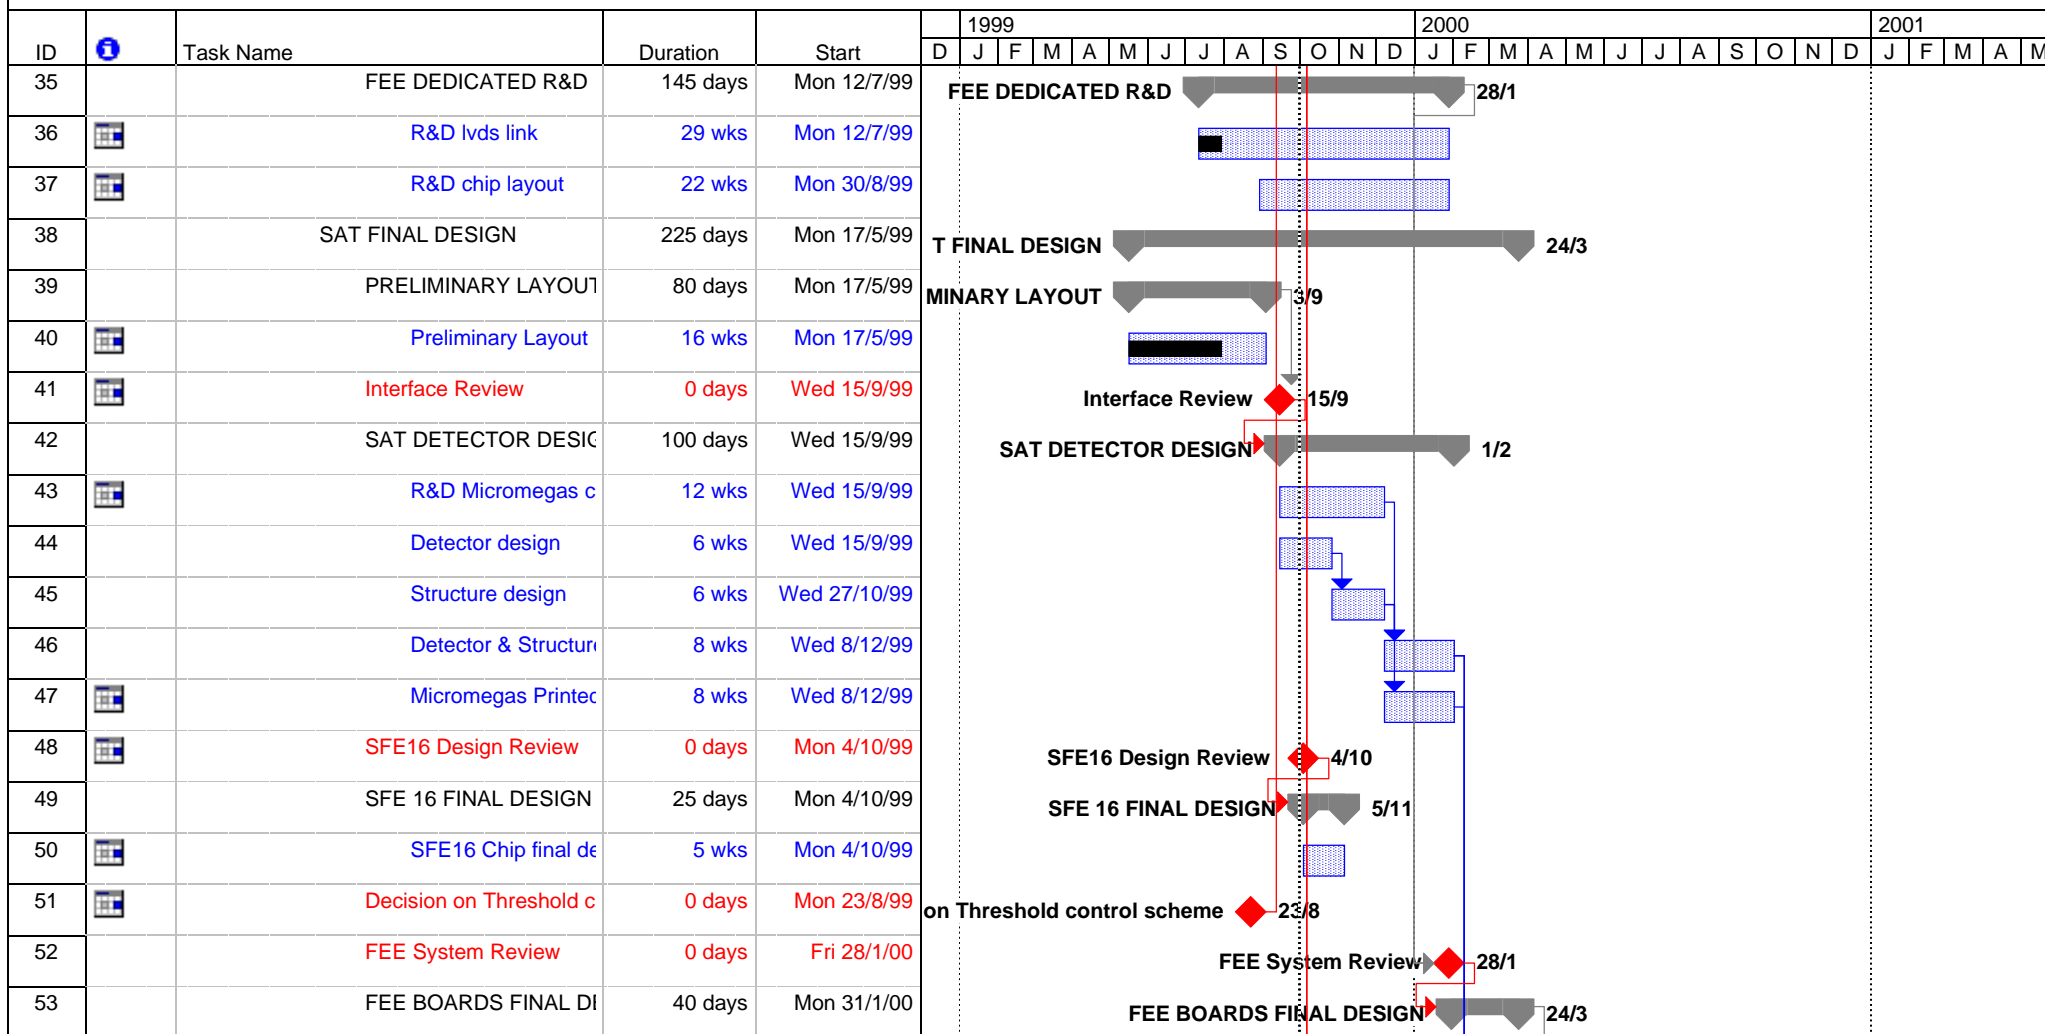

Project: Compass Spectrometer Date: Mon 2/8/99 Co-ordinator: Gerhard Mallot /CERN	Task		Summary		Rolled Up Progress	
	Split		Rolled Up Task		External Tasks	
	Progress		Rolled Up Split		Project Summary	
	Milestone		Rolled Up Milestone			

Compass Spectrometer / CERN


Thu 30/9/99

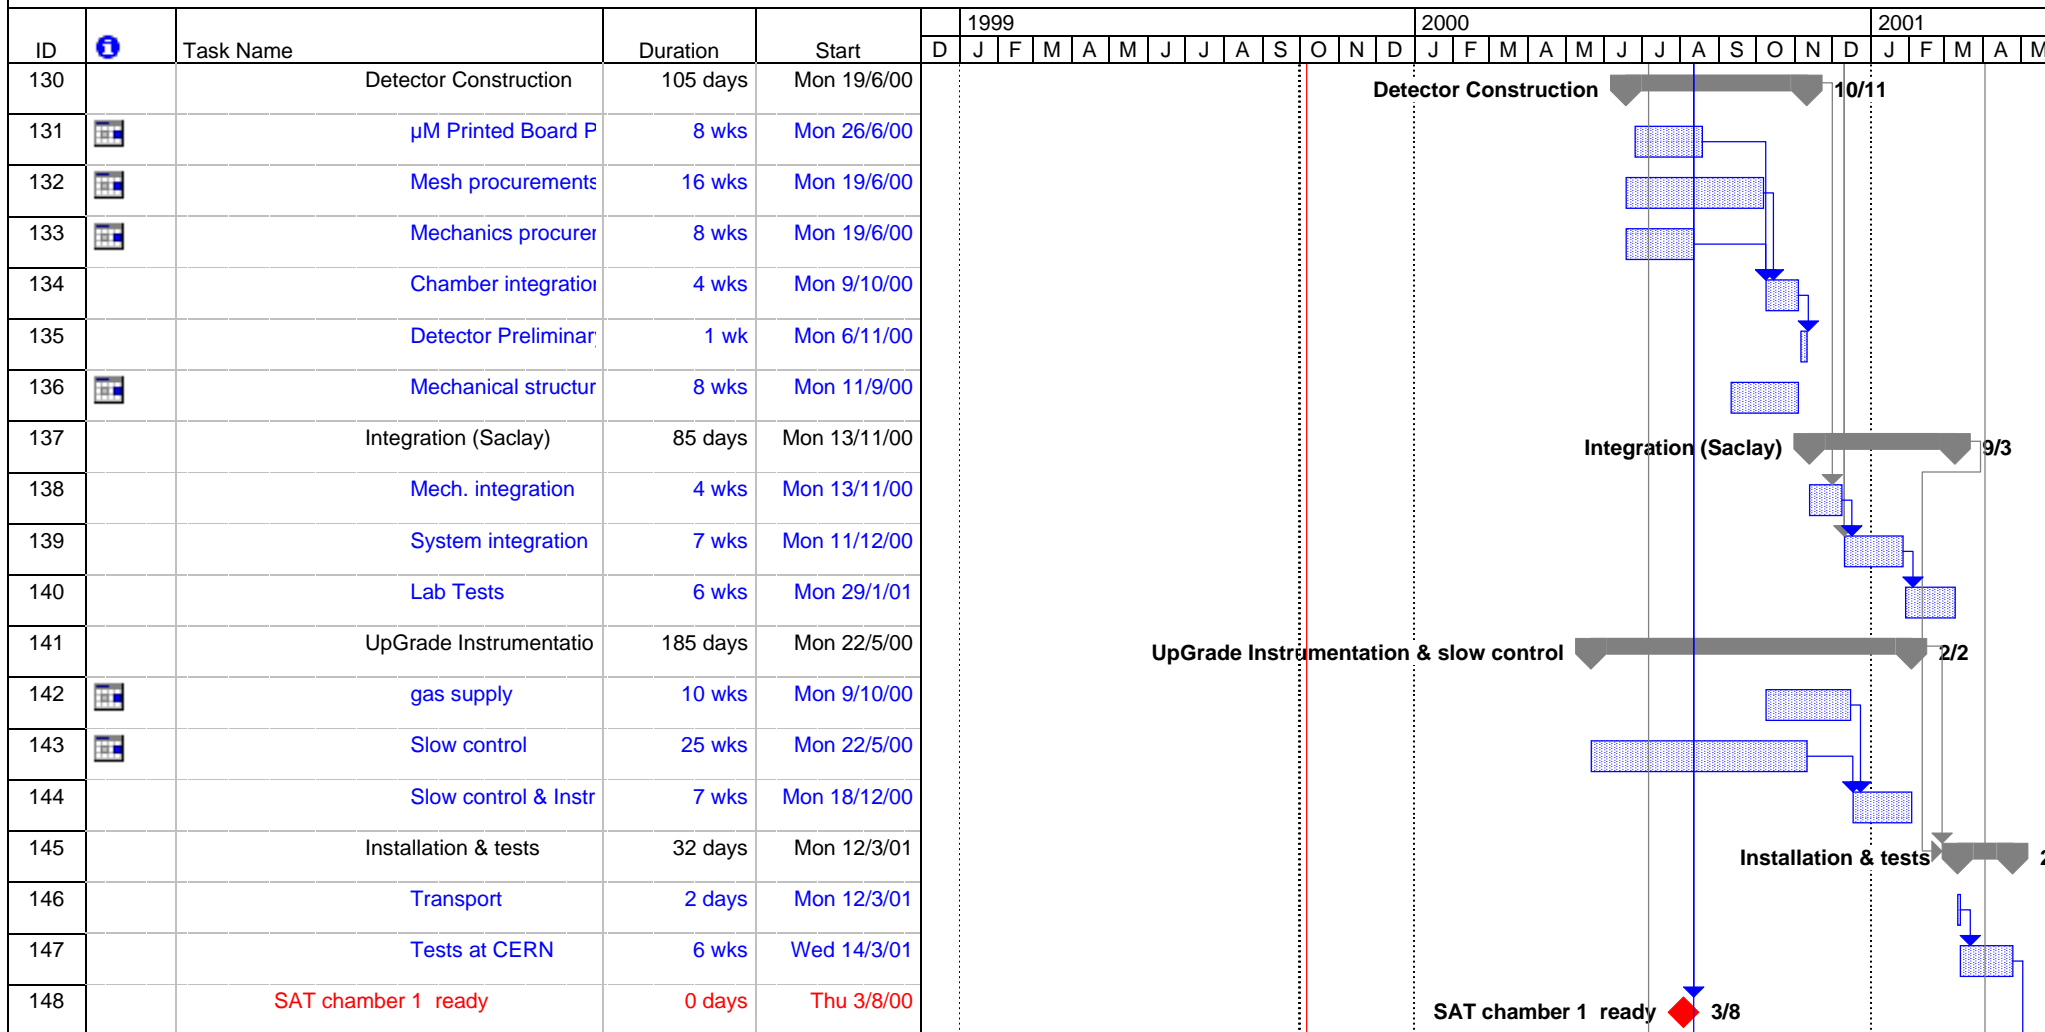


Project: Compass Spectrometer Date: Mon 2/8/99 Co-ordinator: Gerhard Mallot /CERN	Task		Summary		Rolled Up Progress	
	Split		Rolled Up Task		External Tasks	
	Progress		Rolled Up Split		Project Summary	
	Milestone		Rolled Up Milestone			

Compass Spectrometer / CERN


Thu 30/9/99

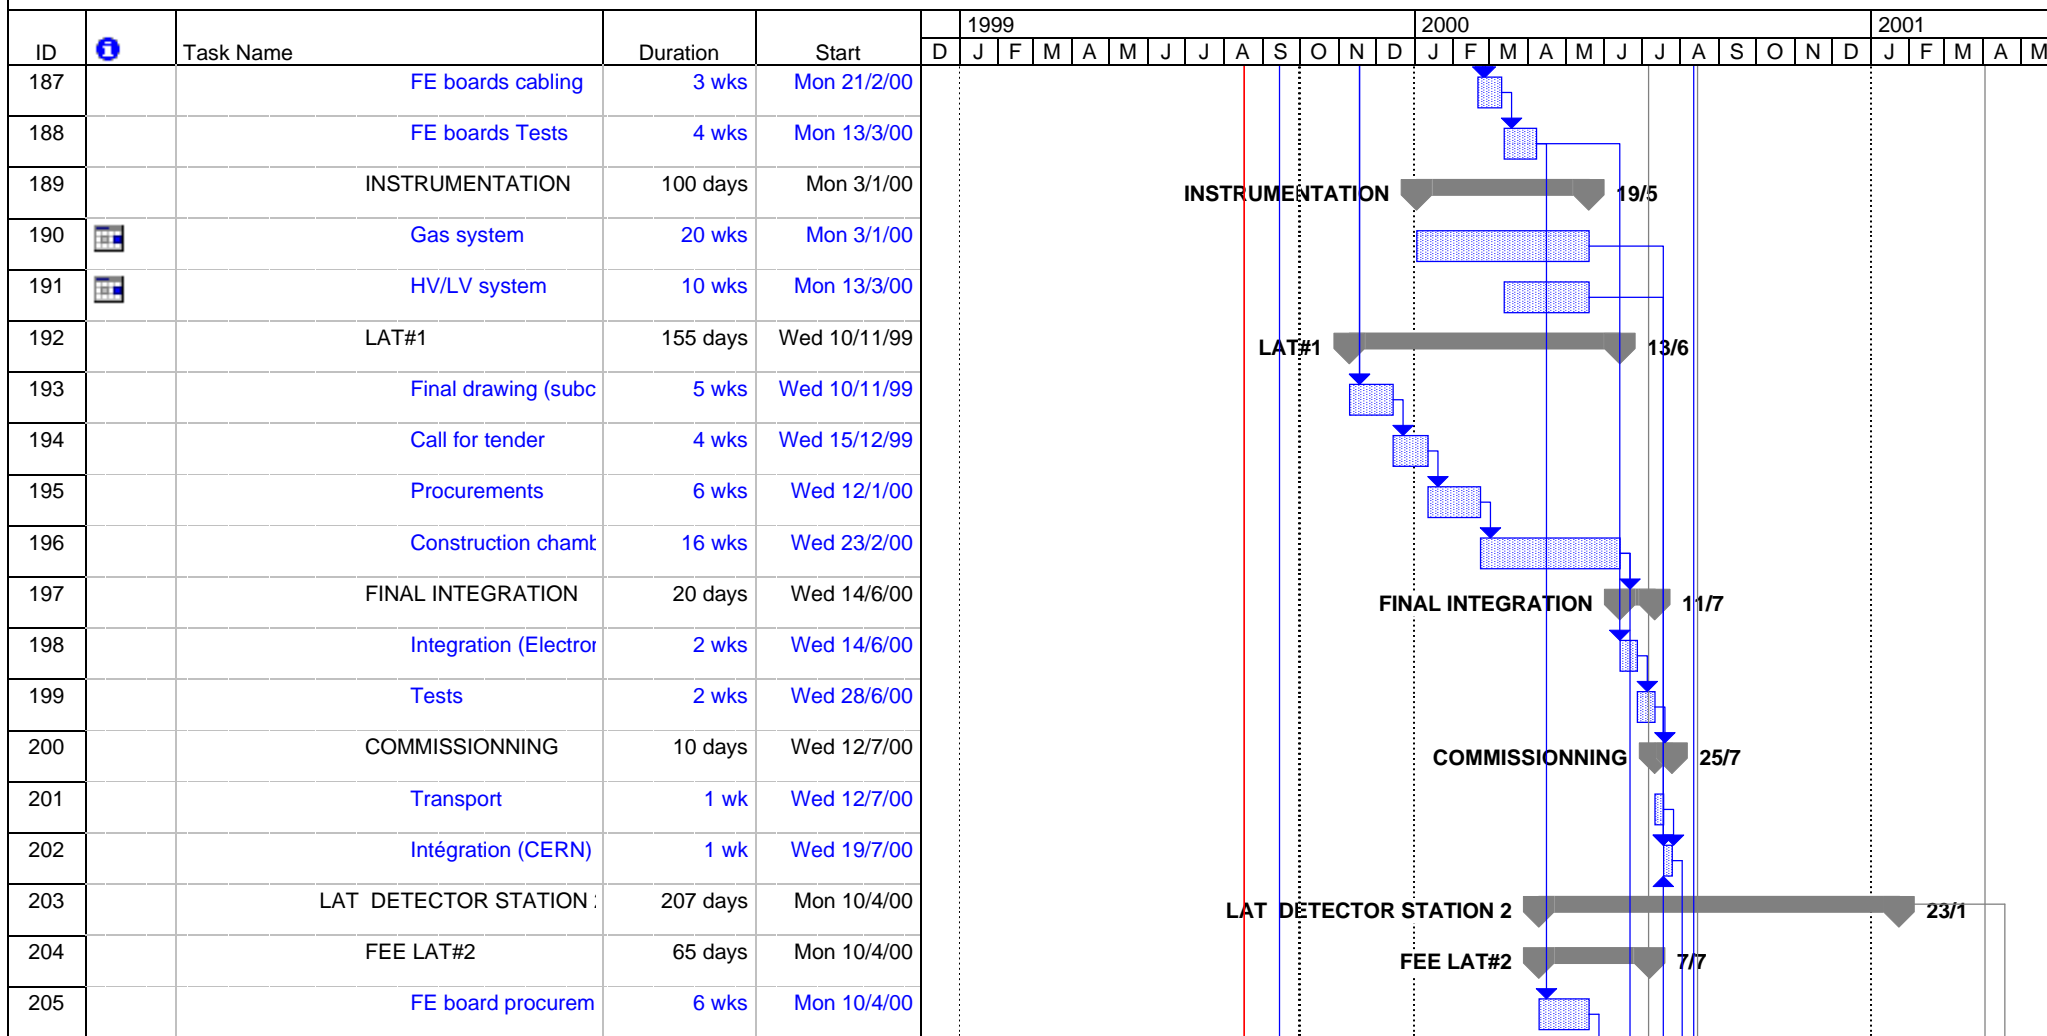

Project: Compass Spectrometer
Date: Mon 2/8/99
Co-ordinator: Gerhard Mallot /CERN




Compass Spectrometer / CERN

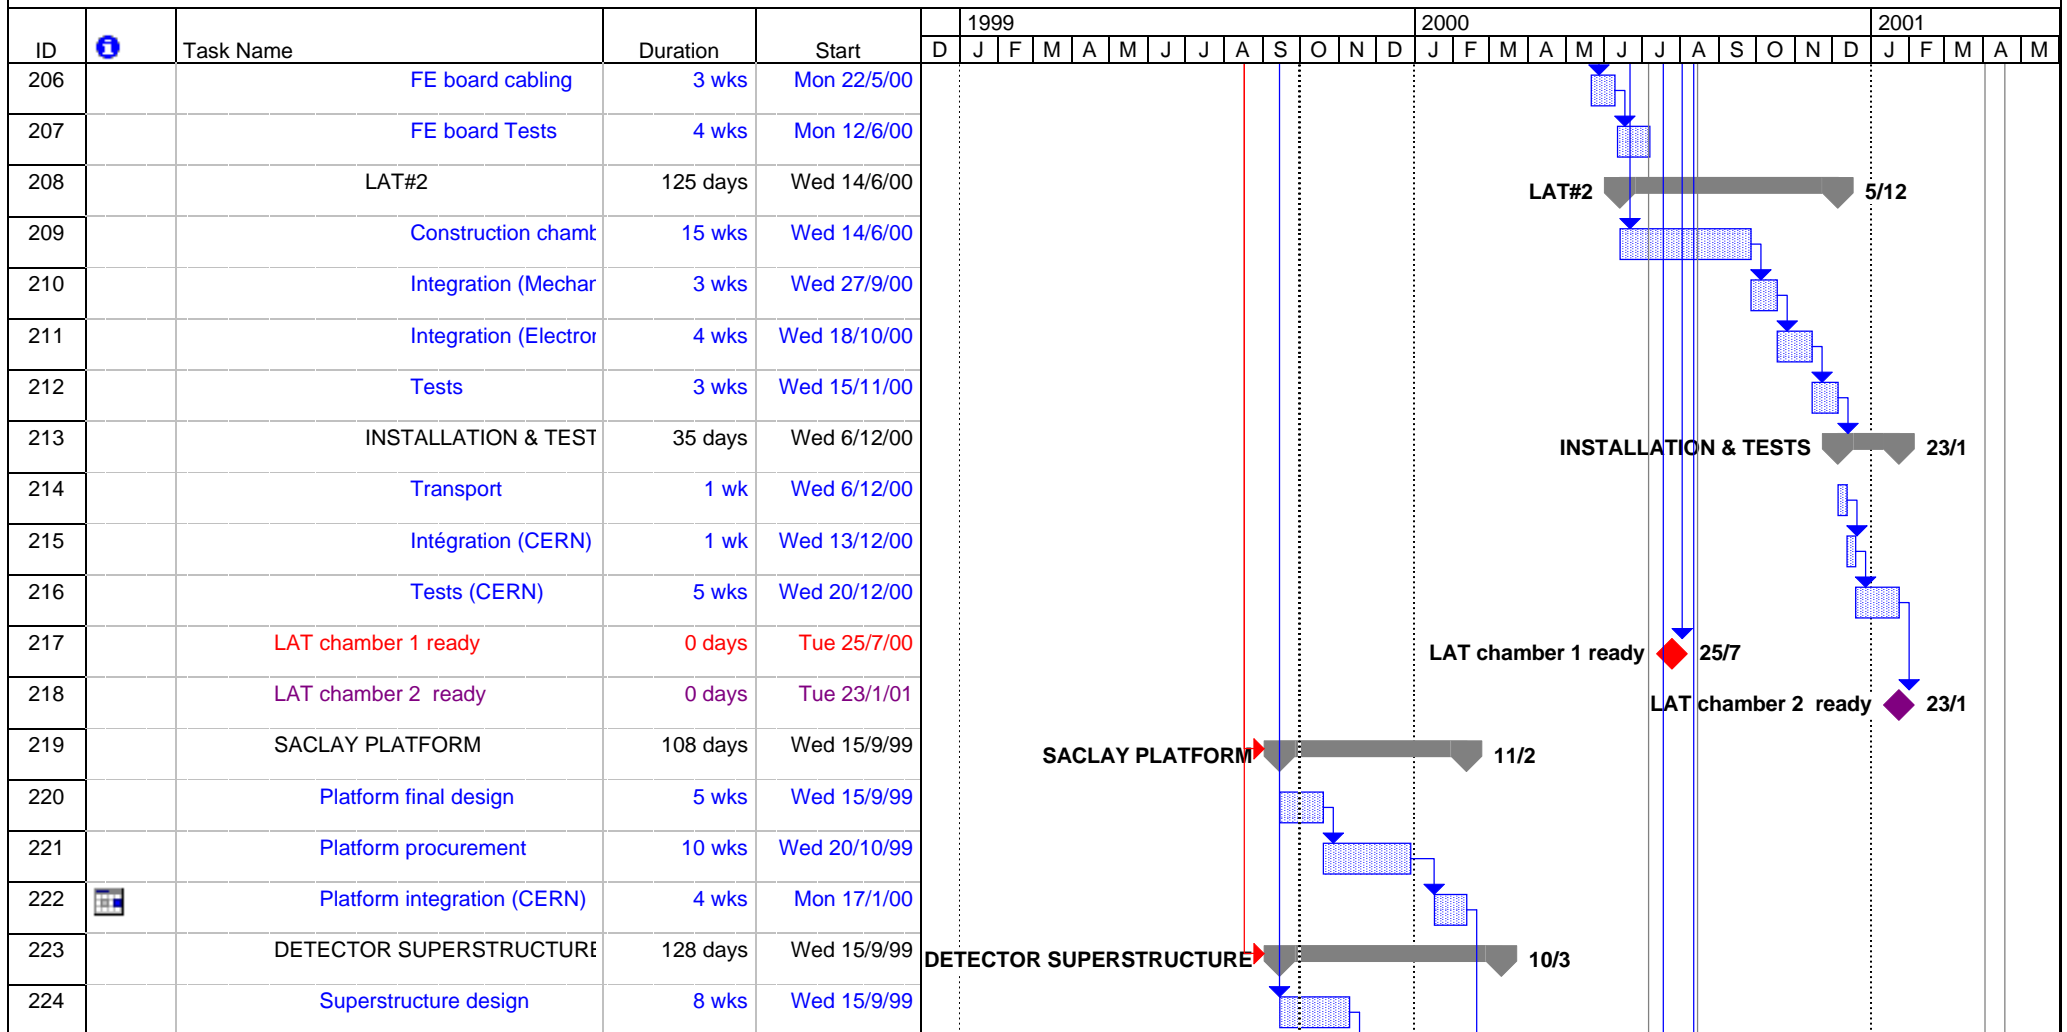

<p>Project: Compass Spectrometer Date: Mon 2/8/99 Co-ordinator: Gerhard Mallot /CERN</p>	<table style="width: 100%;"> <tr> <td>Task </td> <td>Summary </td> <td>Rolled Up Progress </td> </tr> <tr> <td>Split </td> <td>Rolled Up Task </td> <td>External Tasks </td> </tr> <tr> <td>Progress </td> <td>Rolled Up Split </td> <td>Project Summary </td> </tr> <tr> <td>Milestone </td> <td>Rolled Up Milestone </td> <td></td> </tr> </table>	Task	Summary	Rolled Up Progress	Split	Rolled Up Task	External Tasks	Progress	Rolled Up Split	Project Summary	Milestone	Rolled Up Milestone	
Task	Summary	Rolled Up Progress											
Split	Rolled Up Task	External Tasks											
Progress	Rolled Up Split	Project Summary											
Milestone	Rolled Up Milestone												

Compass Spectrometer / CERN


Thu 30/9/99

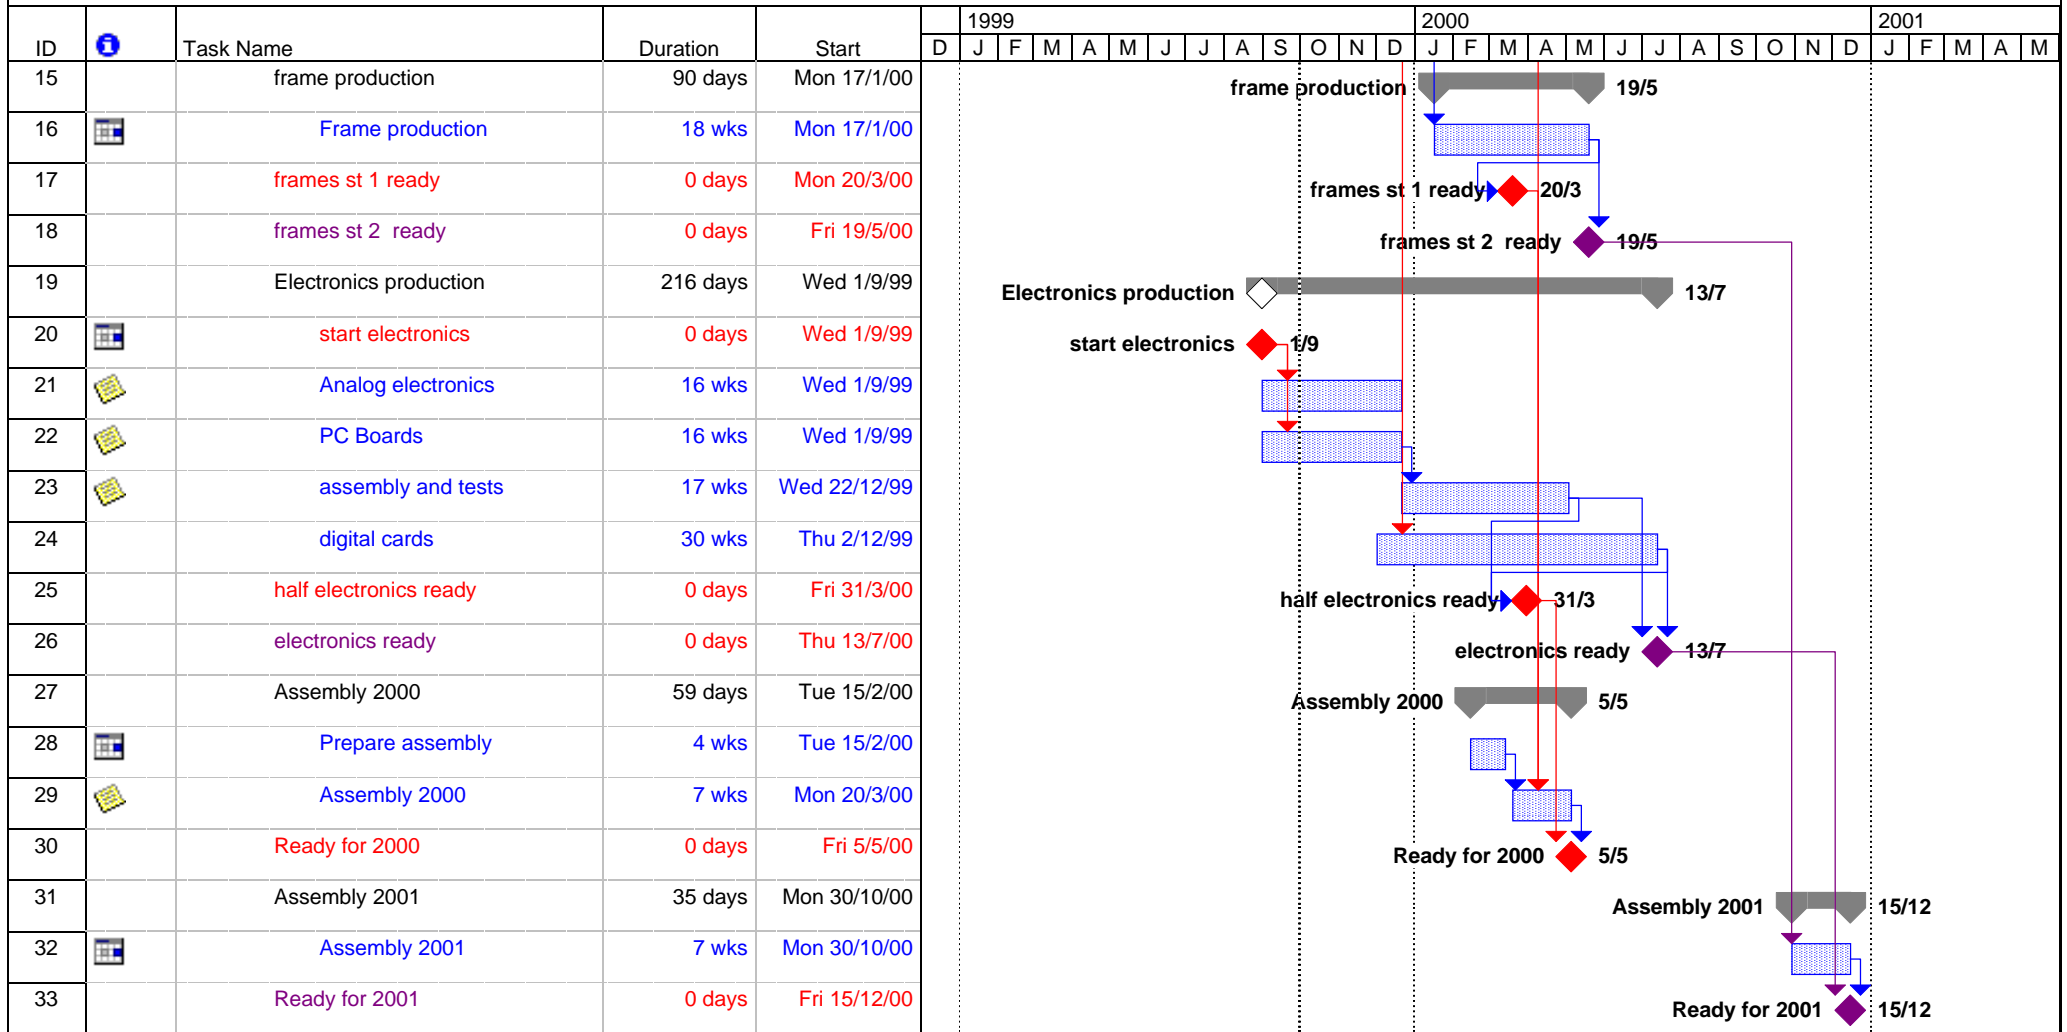

Project: Compass Spectrometer Date: Mon 2/8/99 Co-ordinator: Gerhard Mallot /CERN	Task		Summary		Rolled Up Progress	
	Split		Rolled Up Task		External Tasks	
	Progress		Rolled Up Split		Project Summary	
	Milestone		Rolled Up Milestone			

Compass Spectrometer / CERN


Thu 30/9/99

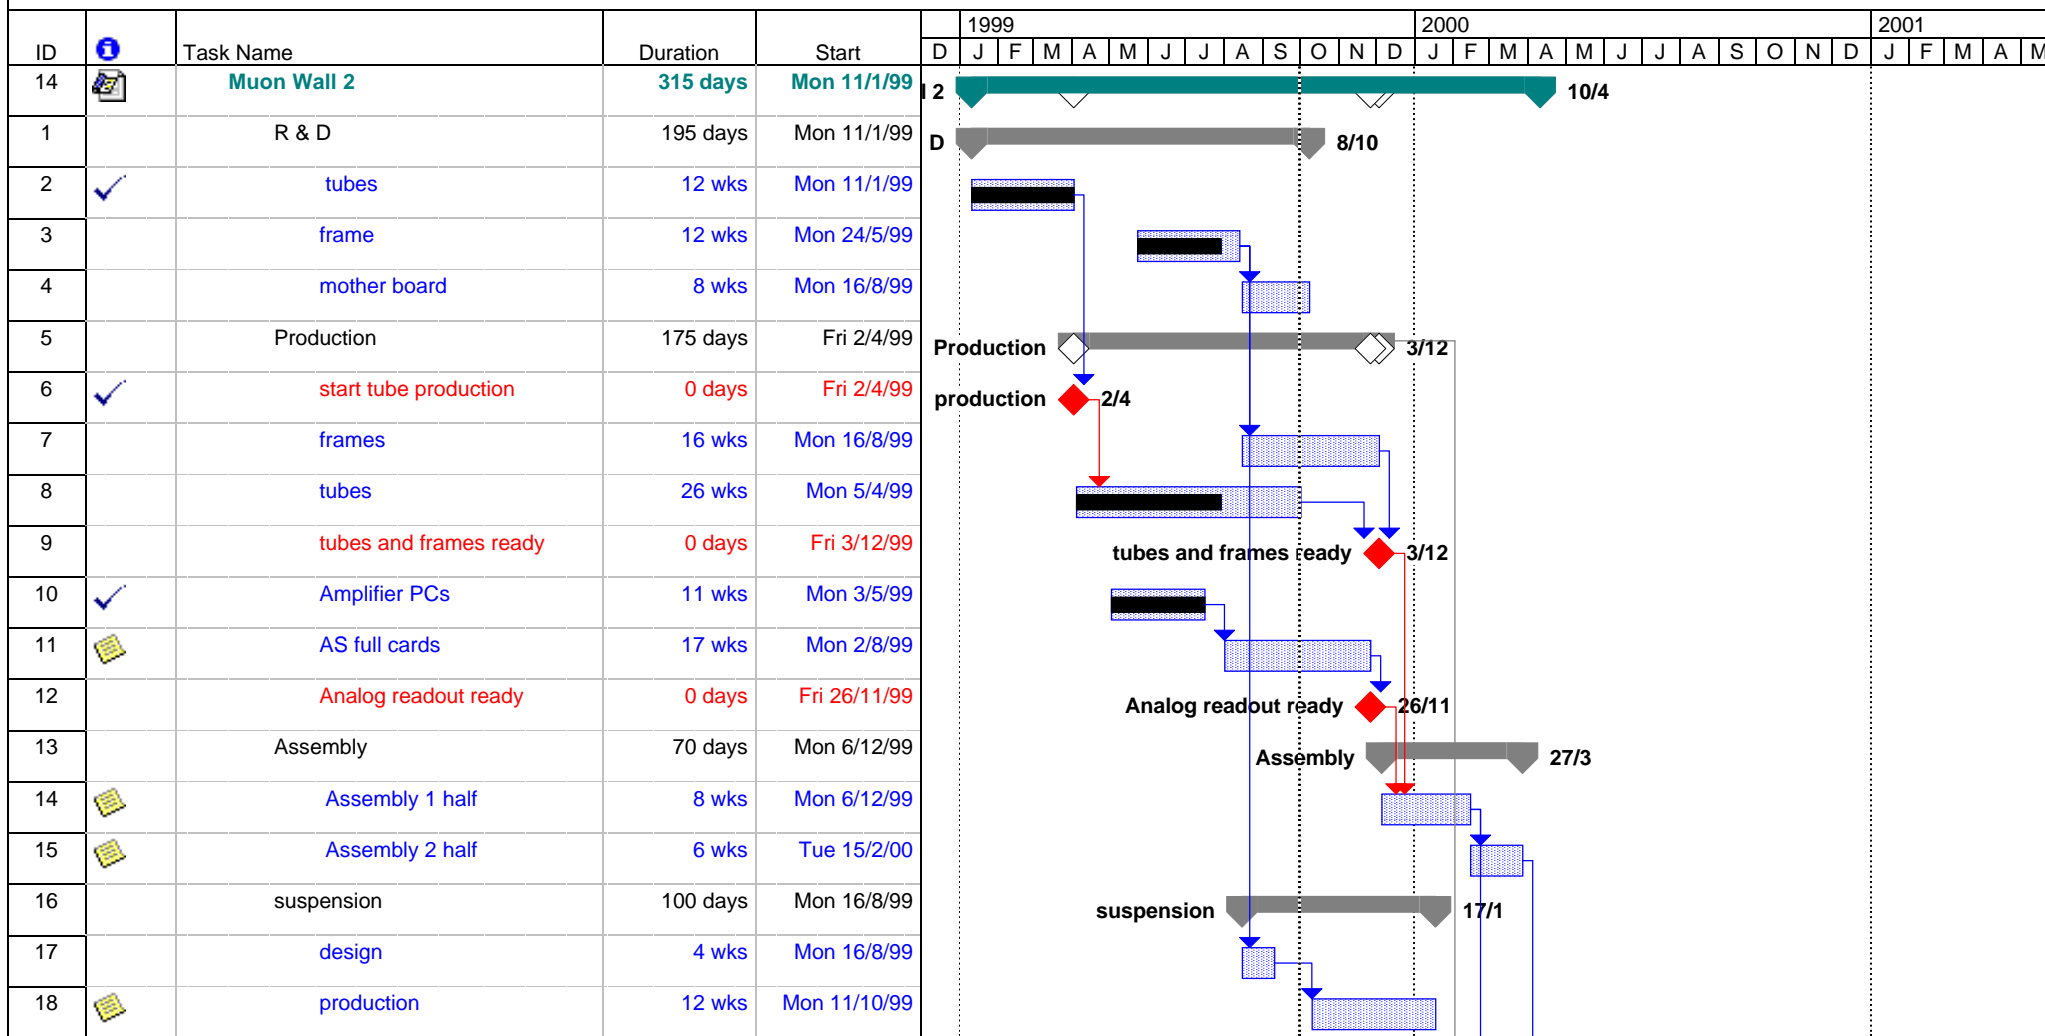

Project: Compass Spectrometer Date: Mon 2/8/99 Co-ordinator: Gerhard Mallot /CERN	Task		Summary		Rolled Up Progress	
	Split		Rolled Up Task		External Tasks	
	Progress		Rolled Up Split		Project Summary	
	Milestone		Rolled Up Milestone			

Compass Spectrometer / CERN


Thu 30/9/99

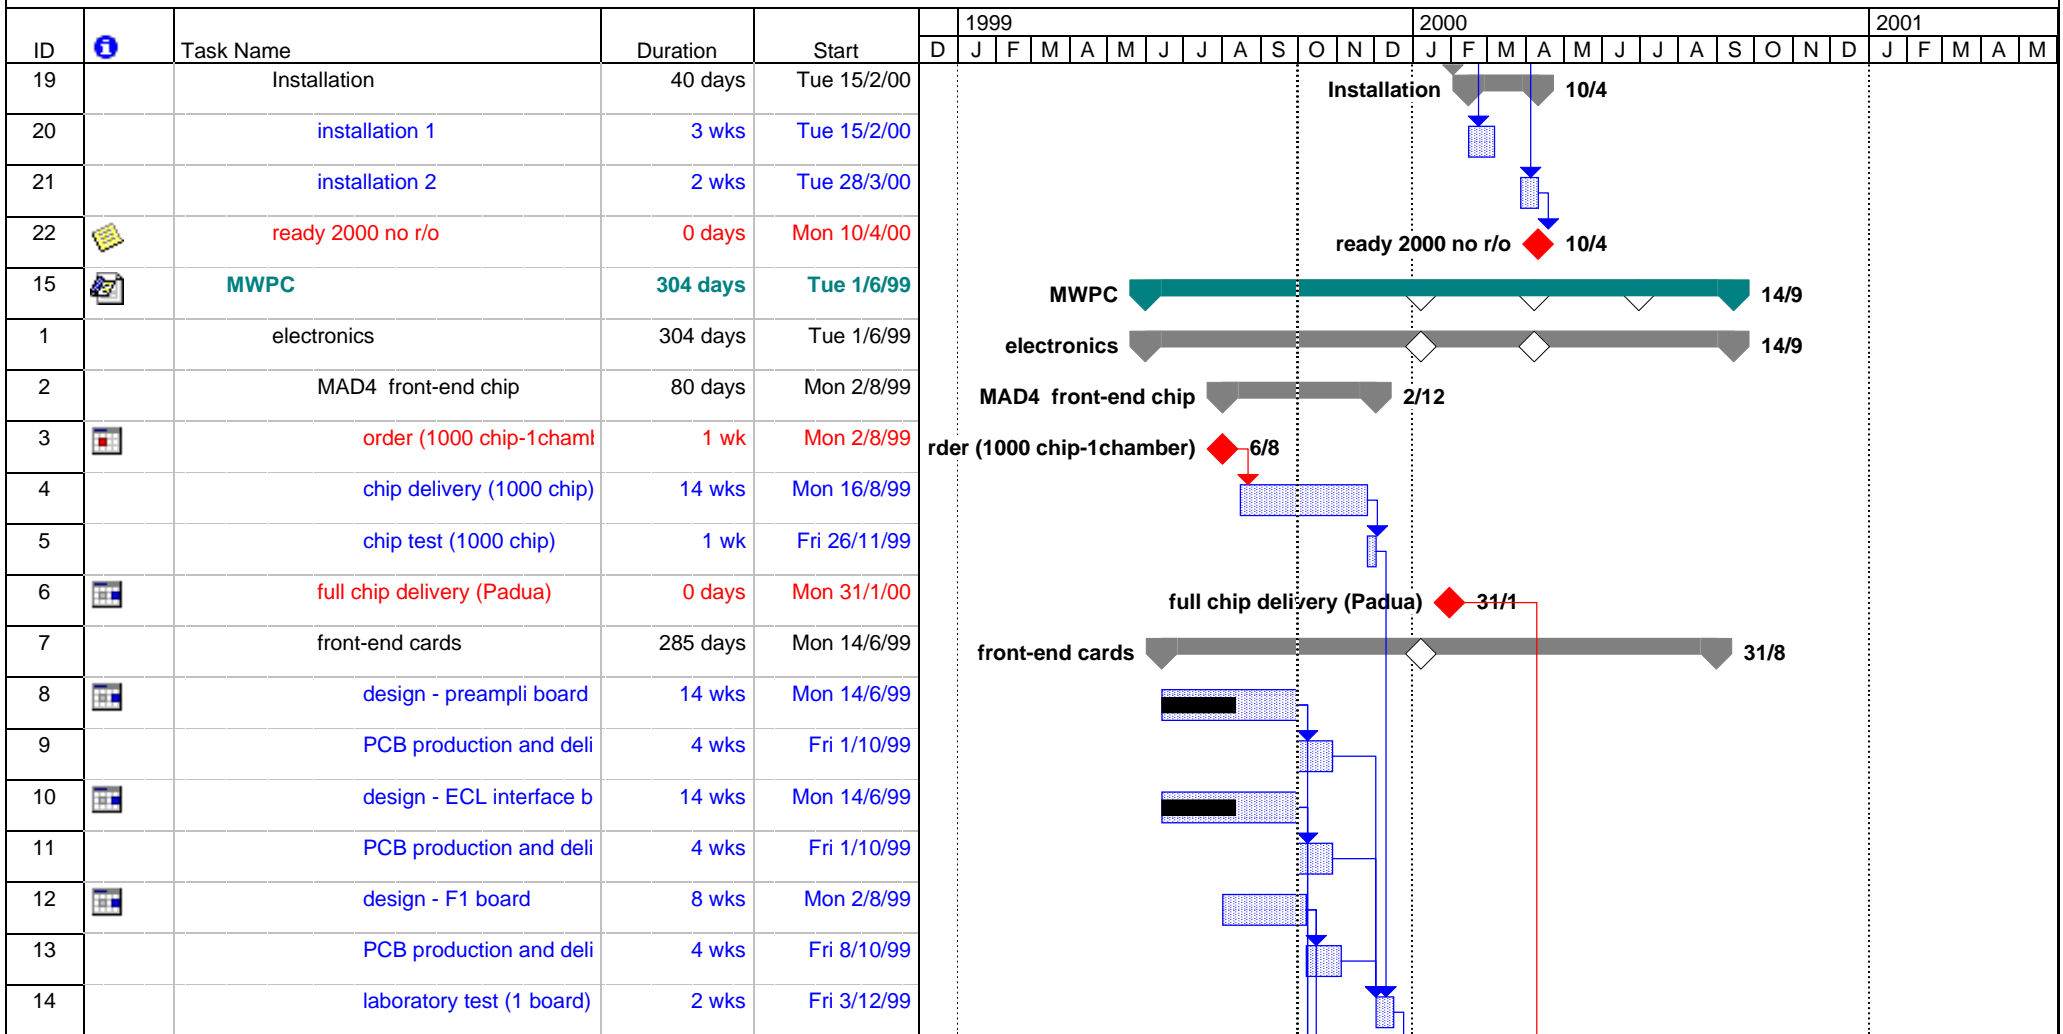

Project: Compass Spectrometer
Date: Mon 2/8/99
Co-ordinator: Gerhard Mallot /CERN

Compass Spectrometer / CERN


Thu 30/9/99

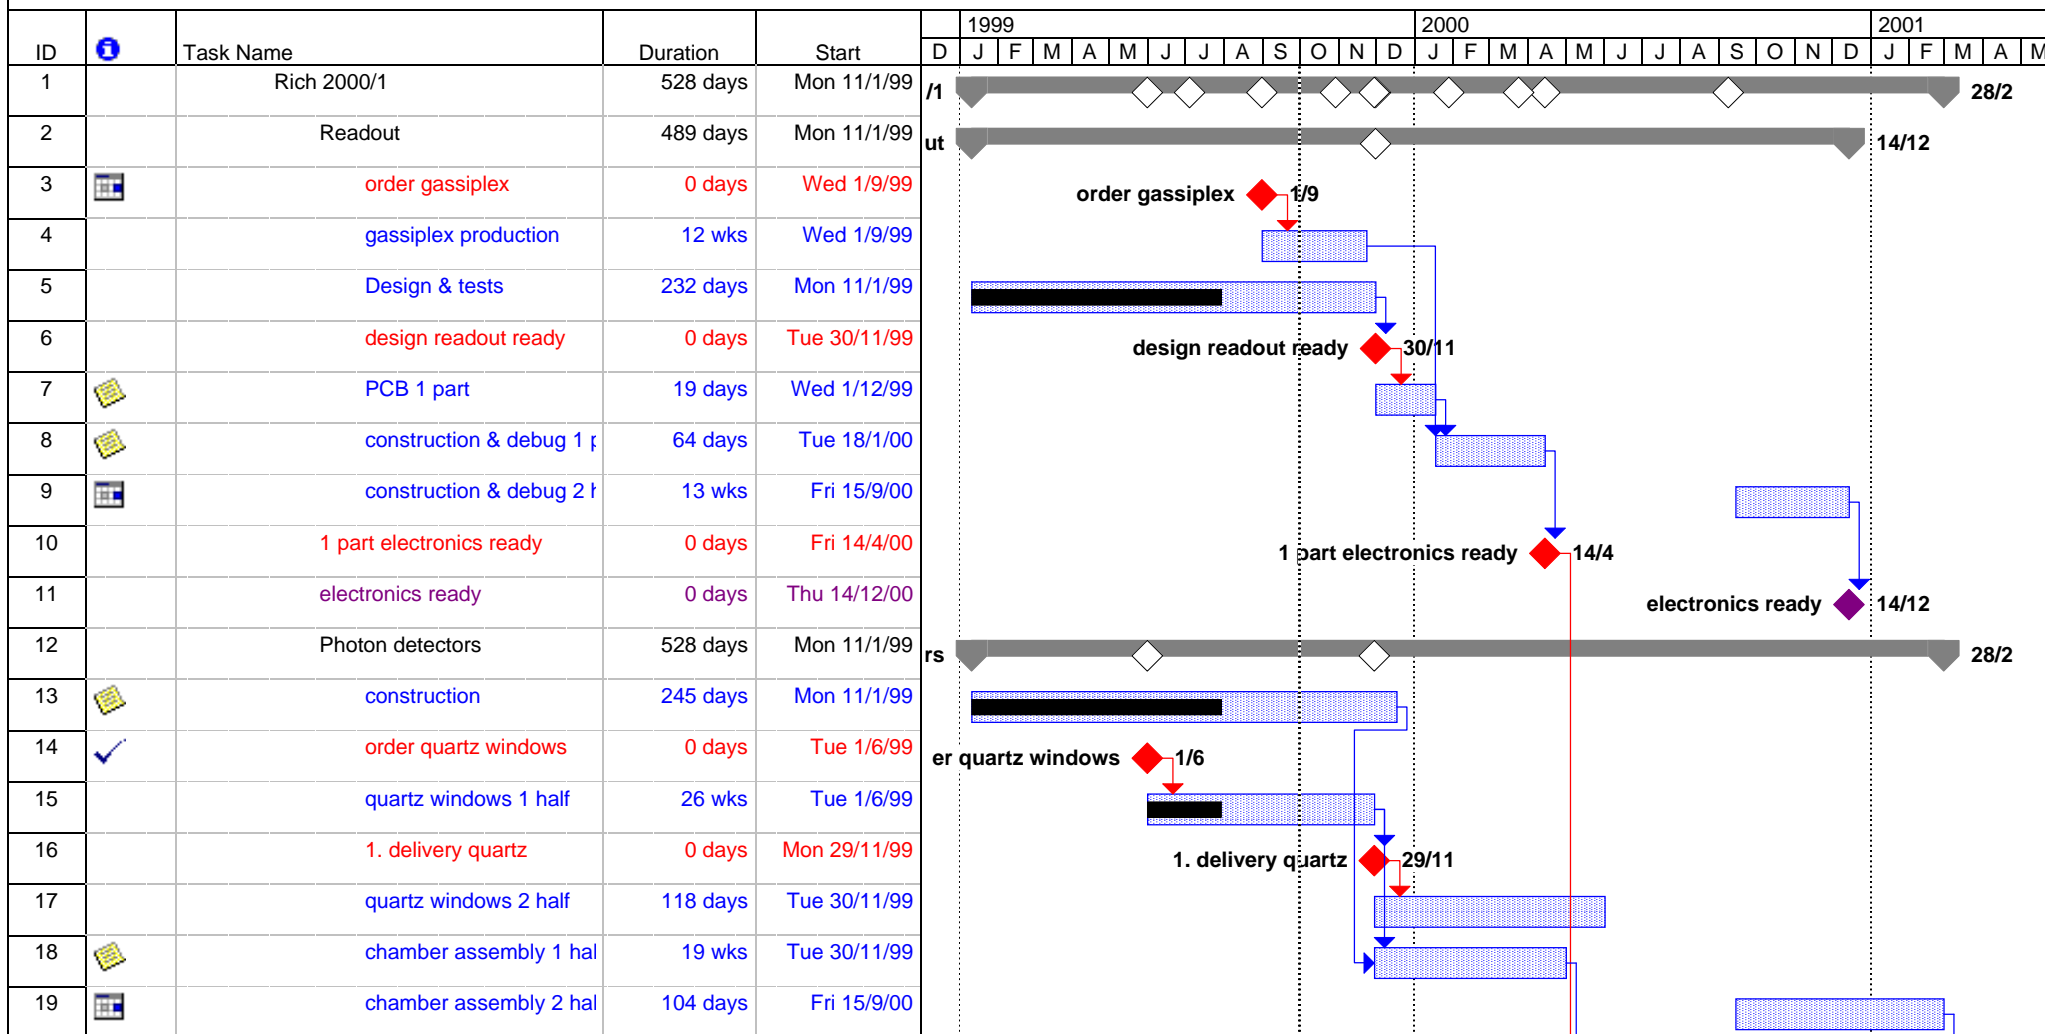

Project: Compass Spectrometer Date: Mon 2/8/99 Co-ordinator: Gerhard Mallot /CERN	Task		Summary		Rolled Up Progress	
	Split		Rolled Up Task		External Tasks	
	Progress		Rolled Up Split		Project Summary	
	Milestone		Rolled Up Milestone			

Compass Spectrometer / CERN

Thu 30/9/99

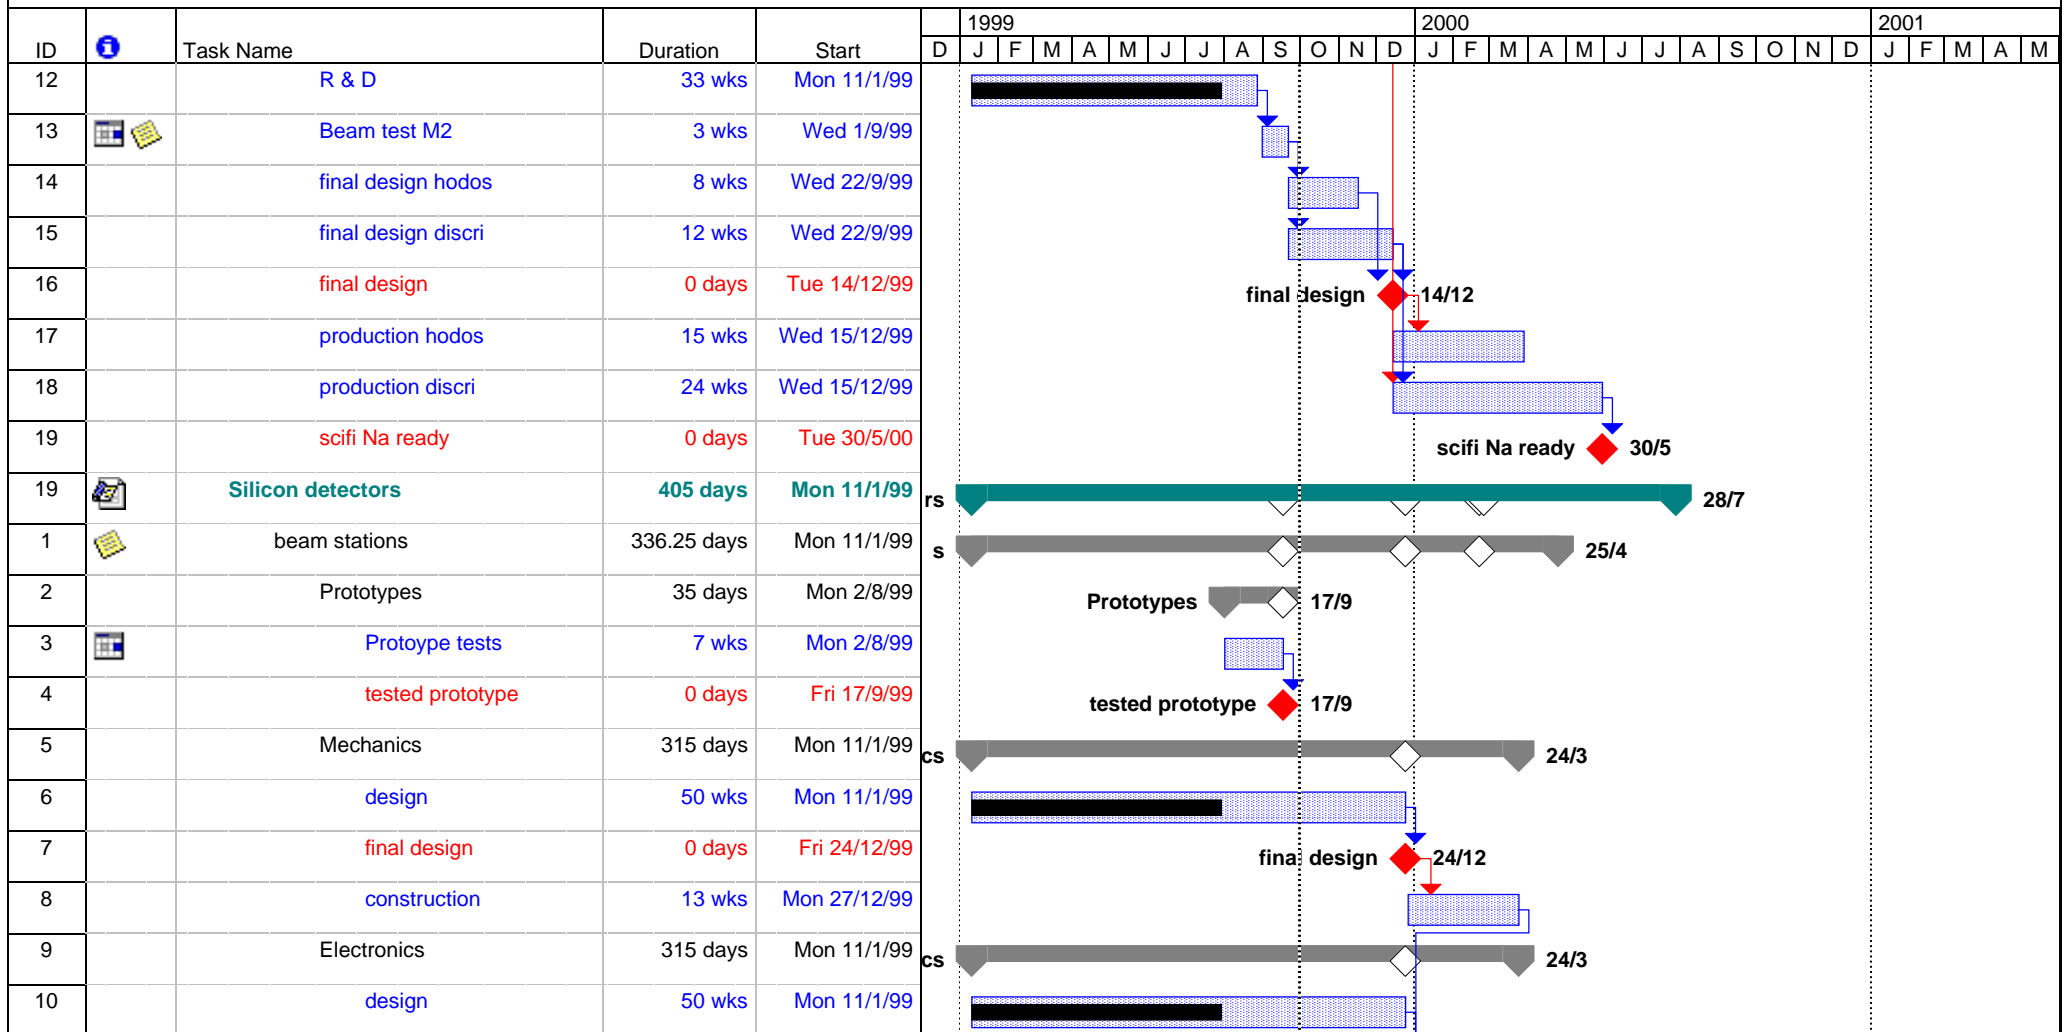


Project: Compass Spectrometer
 Date: Mon 2/8/99
 Co-ordinator: Gerhard Mallot /CERN

Task		Summary		Rolled Up Progress	
Split		Rolled Up Task		External Tasks	
Progress		Rolled Up Split		Project Summary	
Milestone		Rolled Up Milestone			

Compass Spectrometer / CERN

Thu 30/9/99

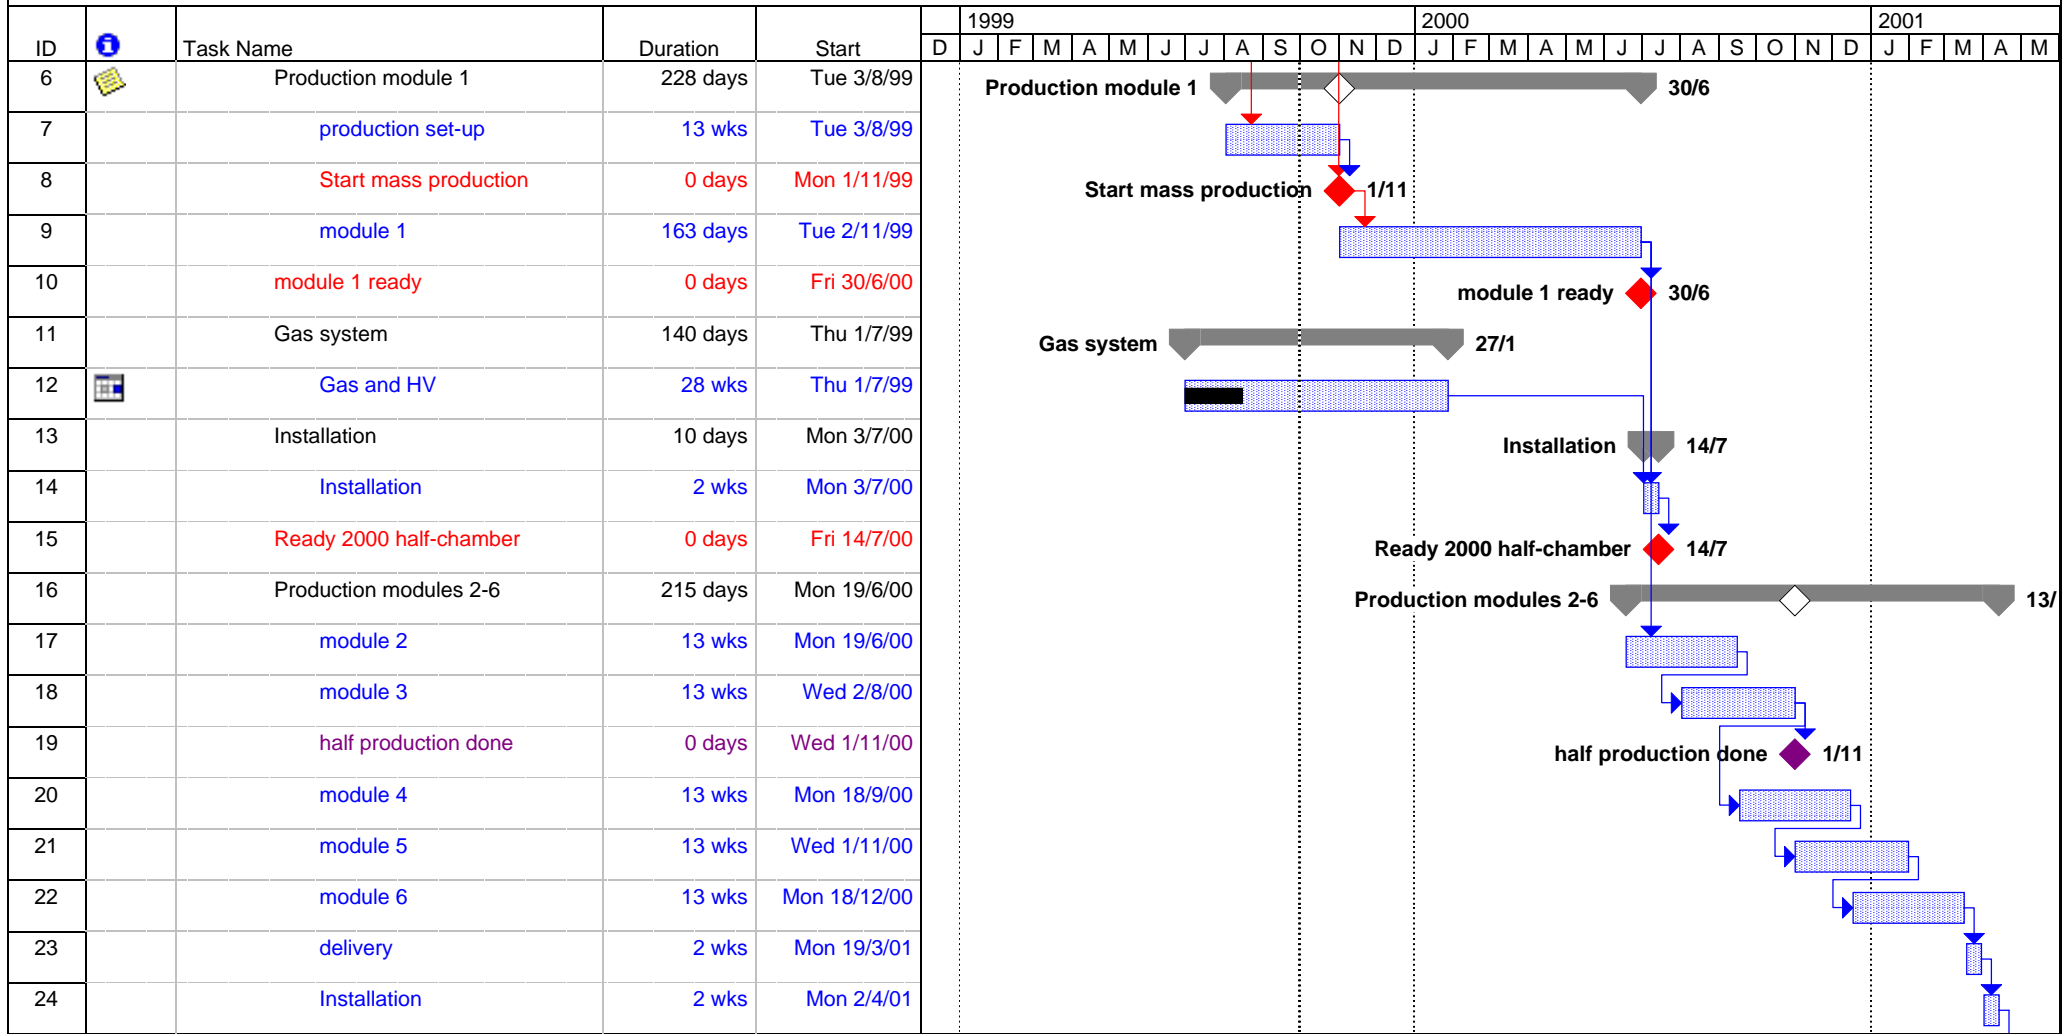

Project: Compass Spectrometer Date: Mon 2/8/99 Co-ordinator: Gerhard Mallot /CERN	Task		Summary		Rolled Up Progress	
	Split		Rolled Up Task		External Tasks	
	Progress		Rolled Up Split		Project Summary	
	Milestone		Rolled Up Milestone			

Compass Spectrometer / CERN

Thu 30/9/99

ID		Task Name	Duration	Start	1999												2000												2001				
					D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A
25		Ready 2001	0 days	Fri 13/4/01																									Ready 2001 13/				



Project: Compass Spectrometer Date: Mon 2/8/99 Co-ordinator: Gerhard Mallot /CERN	Task	Summary	Rolled Up Progress
	Split	Rolled Up Task	External Tasks
	Progress	Rolled Up Split	Project Summary
	Milestone	Rolled Up Milestone	
